
COMMON ALTITUDE

TEAM AND CO-PRODUCER DISCUSSION

Paid scopes, roles and delivery requirements.

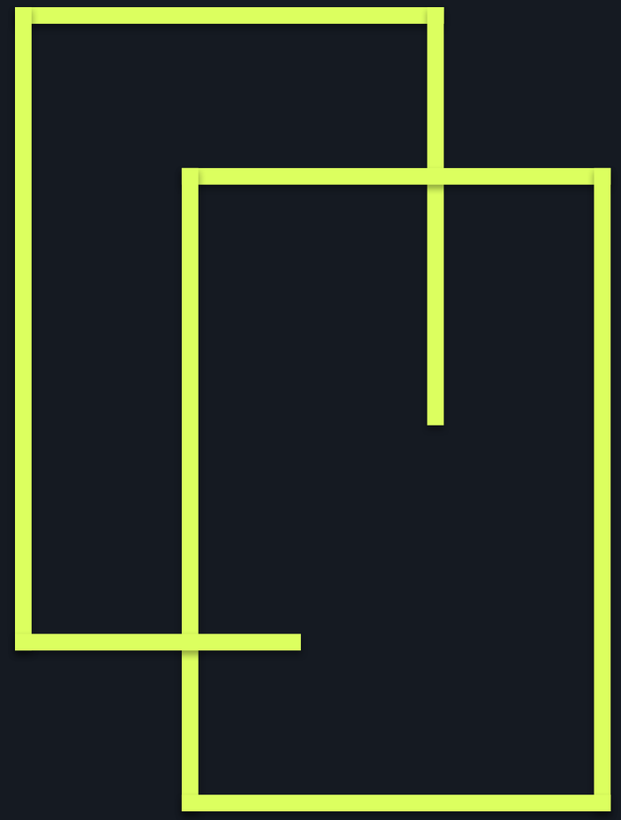

ORIGINAL CONCEPT GRAPHIC

Proposed founding functions

Hours, fees, availability and authority still need agreement.

Artistic + relationships

Curatorial thesis, artists, galleries and market credibility.

Product + program

Digital/service requirements, evidence and cross-functional coordination.

Brand + design

Positioning, identity and coherent physical/digital communication.

First specialist roles

The project needs experienced delivery, collector sales and finance leads.

Executive producer

Comparable complex-venue delivery. Authority and stop rights.

Collector lead

Qualified demand, appointments, seller conversion and service.

Finance/controller

Cash, restrictions, contracts, reconciliation and independent challenge.

Fees, scope and additional bonuses

Agree funded work first. Define any performance or profit participation separately.

- No indefinite unpaid-production expectation.
- Classification, fees, rights, milestones and cancellation agreed.
- Founder equity and an event bonus are different matters.

Paid discovery stage

Begin work only after agreeing the scope and securing usable funds.

$75,000

Discovery underwriting target

$70,000

Defined work envelope

6 weeks

Proposed evidence/decision period

Core delivery fee budgets

These proposed amounts need contracts, hours and worker-classification review.

$260,000

Core-team delivery fees

$200,000


Artist/program fees

$1,550,000

Total proposed core cost

Proposed allocation of 60 spaces

Site evidence must support the footprint. Smaller and larger options need separate budgets.

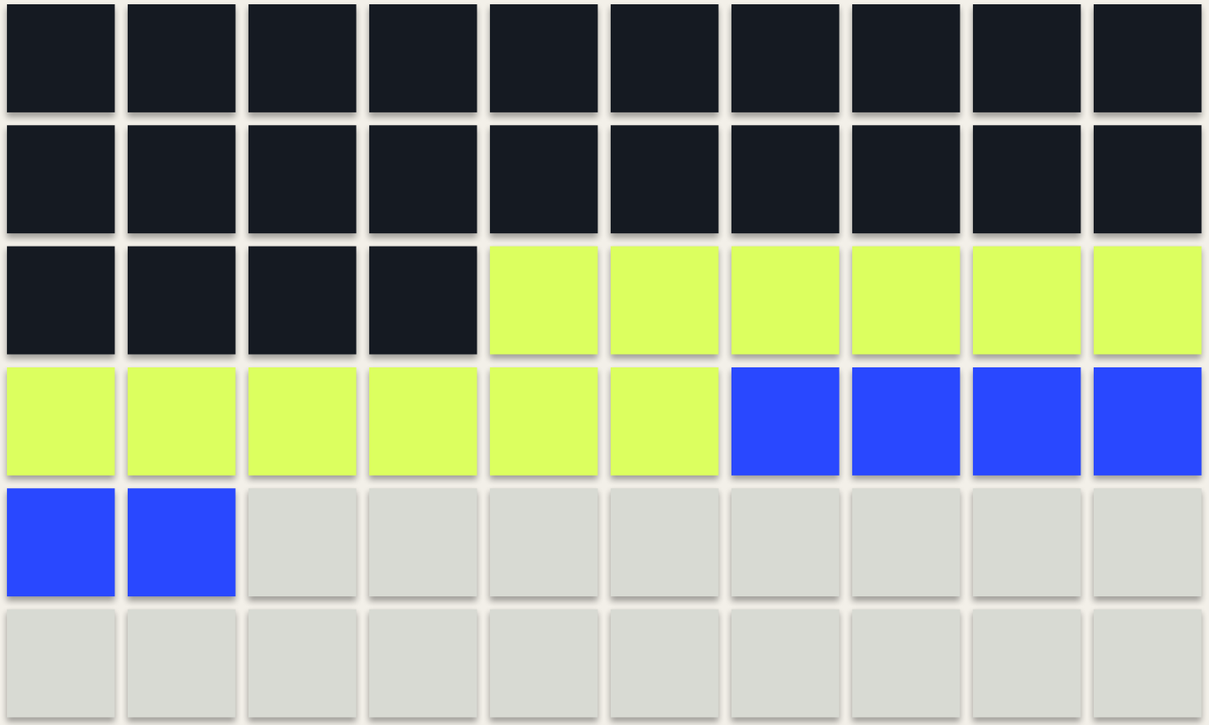

24 Gallery rooms

12 Artist salons

6 Signature briefs

18 Learning, common and support

PROPOSED PROGRAM FUNCTIONS / SITE SURVEY PENDING

Professional candidates

The project has appointed none of these candidates.

Two Parts

Potential production discovery.

Jensen Hughes

Potential local code/accessibility/fire scope.

UOVO Denver

Potential art-handling/logistics scope.

Funding and approval sequence

Site evidence, usable cash and accepted responsibilities control the schedule.

G0–G1

Fund discovery. Establish site feasibility.

G2–G3

Accept delivery roles. Prove launch finance/site path.

G4–G5

Fund/clear program and authorize build.

G6–G7

Rehearse, inspect and open only ready approved areas.

Preview, public days and close

The proposed week runs August 9–15, 2027. Budget preparation and restoration separately.

PREVIEW

Orientation and professional attention.

PUBLIC

Five days of free core art and optional deeper programs.


CLOSE

Art care, restoration, settlement and learning.

Role and capacity discussion

A paid discovery scope would define competence, availability, cost, authority and risk.

- Bring comparable delivered-work evidence and references.
- Identify the conditions you need to deliver well.
- Agree funded scope before recruitment or public credit.



Planning records and role agreements

The package includes 365 daily actions, 53 weekly records and finance, program and operating documents.

Candidate biographies do not establish capacity or willingness.

This deck creates no staffing, fee, equity or profit-share agreement.

Actual accepted roles and private counterpart details belong in controlled operational records.
